#### SPLOST MONTHLY REPORT 4/1/2023

#### 1. Change Order Report

• Revised monthly report (see 1-page attachment)

#### 2. Construction & Design Schedule

• Revised pre-construction schedule (see 1-page attachment)

#### 3. Current Construction

#### West Broad Street Campus

• Dr. Hooker is reviewing the District needs, ACC and community requests for the best use of West Broad Campus.

#### Clarke Middle School

- GA DOE site approval received May 24, 2022
- Architect GA DOE building plan approval submitted on May 16, 2022
- Construction Document kick off meeting help with Design team on May 24, 2022
- Meeting held with Grade levels and Specials teachers on August 2, 2022 to review 40% drawings for their spaces
- Next LBC meeting held on October 19, 2022. Reviewed final plan, site components and interior finish schedule/color pallet
- Drawings to be advertised for bid on November 1, 2022
- General Contractor construction contract approved by the Board at the December 15<sup>th</sup>, 2022 BOE meeting with Grahl Construction for the amount of \$55,825,544
- LDP meeting with ACC held on 1-20-23
- GC mobilized on site with Phase 1 erosion control measures in progress.
- Submittals for electrical switchgear and panels have been submitted and approved for order. Lead time is 72 weeks
- Phase 1 Clearing and Grubbing activities complete
- Excavation for building pad and retaining walls is complete
- Phase 1 Footing installation in progress
- Phase 1 underground plumbing in progress
- Modular units being delivered to the site for August 2023 occupancy

#### • Board Office Renovation- Piedmont College Property Prince Ave.

• December 21, 2021 substantial completion date achieved for 1950 & 1980's building. Move in process of District offices occurred December

- 18-31, 2021. Chapel/Board Room space completed for February 3, 2022 BOE work session
- Survey of the house facing Hill Street and Prince Ave. complete and submitting the revised plat and rezoning application to ACC in progress

#### Cedar Shoals Field House

- Board approve Construction contract with Grahl Construction at May 2022 Board meeting for \$5,539,125
- GC mobilized on site May 31, 2022
- Site storm work 98% complete
- Water and sewer tap complete
- Foundation work is 100% complete
- Underground plumbing work is complete
- Lower level slab on grade poured
- Structural steel installation is complete, steel floor decking installed
- Upper level slab is complete
- Lower and Upper level CMU walls are complete
- Overhead HVAC, Electrical and plumbing rough ins are complete
- Exterior brick installation complete on all elevations
- Electrical transformer set and energized
- Water vault installed
- Gas line installed
- Exterior windows installed
- Priming and painting of interior walls in progress
- Roof soffit and fascia installation are complete
- Metal roof panel installation is complete
- Exterior concrete steps, ramps and sidewalk installation are complete
- Outside make up air unit has been delivered and installation is in progress
- Target Substantial completion date is April 15 2023

#### • Early Learning Center Eastside (at Old Gaines)

- Students and staff occupied 8 classrooms May 2, 2022
- Remaining classrooms in the Earth shelter were occupied August 1, 2022

#### • ACCA Culinary Program Expansion

- Renovation contract approved at February BOE meeting. Contract amount is \$2,066,000 with Grahl Construction
- Project submittals in progress
- Interior work to begin May 30, 2023

# SPLOST Contingency / Change Order Report

	ELC	Cedar Shoals	Clarke		
Contingency / Change Orders	Gaines	Fieldhouse	Middle		
Established Budget By	RFQ	RFP	RFP		
Approved Guaranteed Maximum Price or Bid		\$5,539,125.00	\$55,825,544.00		
Original Contract Amount	\$2,000,000.00	\$5,539,125.00	\$55,825,544.00		
Executed Change Orders:					
Total Change Orders	\$0.00	\$0.00	\$0.00		
Percentage of Contract Amount	0.00%	0.00%	0.00%		
Revised Contract Amount	\$2,000,000.00	\$5,539,125.00	\$55,825,544.00		

### **SPLOST Construction & Design Schedule**

The intent of this document is to provide anticipated and realized schedules of the current and upcoming SPLOST construction projects

April 1, 2023								
Projects	Current Stage	Advertise By	Pre-Bid Conference	Bids Due	Notification to BOE *			
West Broad Campus	TBD	TBD	TBD	TBD	TBD			
Early Learning Center Eastside	Construction	12/07/21	12/15/21	12/22/21	01/13/22			
Cedar Shoals Field House	Construction	03/18/22	03/31/22	04/19/22	05/12/22			
Clarke Middle School	Construction	11/01/22	11/10/22	12/01/22	12/15/22			
Culinary Program-ACCA	Construction	12/15/22	01/09/23	01/19/23	02/09/23			
CCHS & ELC Roofing Projects	Bid	03/24/23	TBD	04/25/23	05/11/23			
Cedar Shoals Renovation	Design	TBD	TBD	TBD	TBD			

* DATES INDICATED ARE ESTIMA	TES UNTIL PROG	RAMMING AND INI	TIAL DESIGN PHA	ASES ARE COMPLI	ETE
Legend:	Active	Completed		Future	]

#### **CLARKE COUNTY SCHOOL DISTRICT**

# ESPLOST 5 CONSTRUCTION PROGRAM SCHEDULE OF INVESTMENT ACTIVITY Month Ending February, 2023

	ESP5 Activity	Synovus
		Checking
Balance Ending January 31, 2023		\$27,785,529
Receipts:		
Earnings:		
Interest Earnings - February 28, 2023		\$6,324
		Ψ 3/32 .
TOTAL REVENUES		
\$6,324		
Expenditures:		
District-Expendable Equipment	\$146,935	
Prince Ave-Professional & Technical Svcs	\$590	
Cedar Shoals Field House-Engineer	\$1,090	
Old Gaines ELC-Expendable Equipment	\$11,830	
Cedar Shoals Field House-Construction	\$686,115	
Old Gaines-Construction	\$9,780	
TOTAL EXPENDITURES		
\$856,340		
ACCOUNT TOTALS - February 28, 2023		\$27,082,449
110000111110111101111111111111111111111		Ŧ=:,==,:. <b>9</b>

## **ESPLOST 5 BUDGET PROJECTIONS AT FEBRUARY 28, 2023**

Notes	Project	Original	Projected	Expenditure	Encumbered	Remaining
Notes	Project	Budget	Budget	Expenditure	Liicamberea	Balance
	Cedar Shoals Field-House	0	6,396,081	4,494,374	1,839,226	62,481
	Technology	20,000,000	18,005,177	17,975,258	29,919	0
	Transportation - Buses	2,500,000	2,473,000	2,104,225	368,775	0
	Board HQ - Prince Av. Renovation	0	8,420,088	8,401,311	18,776	0
	ELC at Old Gaines	0	2,000,000	1,057,909	3,200	938,891
1	Clarke Middle	10,000,000	14,116,821	2,032,912	8,683,876	3,400,034
	HT Edwards Culinary Kitchen	0	2,269,300	74,177	1,035,555	1,159,567
	School Nutrition	300,000	300,000	159,434	0	140,566
	Systems Renewal - Other	0	18,547	2,470	16,077	0
Comple	eted Projects					
	Administration	2,500,000	1,733,901	1,733,901	0	0
	BHL - Mar 2019	10,000,000	17,042,109	17,042,109	0	0
	Board HQ - Exploring Properties	0	23,209	23,209	0	0
2	Board HQ -Prince Av. Purchase	0	5,517,956	5,517,956	0	0
	Cedar Shoals Old Gym - Jul 2020	0	528,948	528,948	0	0
	Cedar Shoals Track - Mar, 2021	2,000,000	1,043,345	1,043,345	0	0
	Clarke Central Softball - Sep 2019	0	446,263	446,263	0	0
	Clarke Central Softball Dugout	0	56,059	56,059	0	0
	Clarke Central Track/Field - Mar, 2021	0	5,283,087	5,283,087	0	0
	Coile - Mar 2019	10,000,000	16,162,136	16,162,136	0	0
	Cosmetology Lab - Dec 2019	0	292,260	292,260	0	0
	Custodial Equipment	300,000	299,549	299,549	0	0
	ELC Kitchen - May 2022	0	1,018,607	1,018,607	0	0
	Gaines Kitchen Floor - Jul 2019	0	39,016	39,016	0	0
	Hilsman - Sep 2019	25,000,000	28,082,480	28,082,480	0	0
3	Hilsman Health Clinic - Sep 2019	0	171,666	171,666	0	0
	HS Basketball Scoreboards	0	62,792	62,792	0	0
	Manufacturing Lab - Feb 2021	0	467,733	467,733	0	0
4	Oglethorpe - Sep 2018	5,000,000	1,511,918	1,511,918	0	0
	Plant Services Truck	0	26,819	26,819		0
	Property Assessments	121,098	121,098	121,098	0	0
	Public Safety Radio - Dec 2020	0	138,505	138,505	0	0
	Storefronts - Sep 2019	0	71,964	71,964	0	0
	Systems Renewal	8,425,000	254,773	254,773	0	0
Project	s not yet commenced					
	Cedar Shoals - Systems	0	0	0	0	0
	District Services	1,700,000	22,707	22,707	0	0
5	Extra Curricular	2,500,000	0	0	0	0
	Old Gaines	0	5,193	5,193	0	0
	School C	0	4,620	4,620	0	0
	Timothy Road	2,500,000	0	0	0	0
	West Broad for ELC	6,000,000	414,131	414,131	0	0
	Contingency	2,153,902	10,412,715	0	0	10,412,715
	PROJECT EXPENDITURE	111,000,000	145,254,571	117,144,912	11,995,405	16,114,255
				Received to		
				Date		
6	Capital Outlay Income	0	9,812,240	9,812,240		
3	Piedmont-Hilsman Clinic	0	171,666	171,666		
7	Sales tax	111,000,000	135,270,665	135,270,665		
	INCOME	111,000,000	145,254,571	145,254,571		

#### Notes

- 1 \$14.13m allocated from ESPLOST 5 to Clarke Middle School new-build. The balance required will be met from ESPLOST 6
- 2 Additional funds of \$2.7m used from the Capital Project Fund 370
- 3 The Hilsman Health Clinic work was managed by the SPLOST Department but not ESPLOST funded. Funding was from the Piedmont Health Foundation
- 4 Oglethorpe was predominantly funded from ESPLOST 4 \$19,467,684
- 5 Extra Curricular funds were re-allocated to High School Athletics
- 6 Capital Outlay income:

	Projected	Received
BHL	1,728,088	1,728,088
Coile	2,343,006	2,343,006
Hilsman	5,741,146	5,741,146
TOTAL	9,812,240	9,812,240

7 Sales tax income based on:

Original 60 months @ \$1,850,000 = \$111,000,000

FINAL Received for the 60 months: \$135,270,665

ESPLOST 5 ran from July, 2017 to June, 2022

#### **CLARKE COUNTY SCHOOL DISTRICT**

# ESPLOST 6 CONSTRUCTION PROGRAM SCHEDULE OF INVESTMENT ACTIVITY Month Ending February, 2023

	ESP6 Activity	Synovus Checking	Synovous Custodial	Invested
Balance Ending January 31, 2023		\$1,672,643	\$659,852	\$91,238,962
Earnings: Interest Earnings/Gains - February 28, 2023		\$23	\$1,058	-\$133,555
Sales Tax - January, 2023				\$2,665,277
TOTAL REVENUES \$2,532,804				
Expenditures:				
Administration-Payroll	\$27,887			
Administration-Copier Charges	\$50			
Administration - Travel	\$295			
Administration-Prof & Technical Svcs	\$2,500			
Administrative-Advertising	\$60			
Technology	\$11,655			
TOTAL EXPENDITURES				
\$42,448				
Transfers & Adjustments				
ACCOUNT TOTALS - February 28, 2023		\$1,628,746	\$660,910	\$93,770,684
				4
TOTAL ESPLOST 6 CASH AND INVESTMENTS				\$96,060,341


#### **CLARKE COUNTY SCHOOL DISTRICT**

#### **ESPLOST 6 CONSTRUCTION PROGRAM**

#### SCHEDULE OF SALES TAX RECEIPTS - Month Ending February, 2023

MONTH	MONTH	ESPLOST	ESPLOST	Current	Averages
COLLECTED	RECEIVED	Sales Tax Receipt	Pro-Rata	Monthly	
				Receipts	
July, 2022	September, 2022	\$2,691,547		\$2,691,547	
August, 2022	October, 2022	\$2,981,243		\$2,981,243	
September, 2022	November, 2022	\$3,043,468		\$3,043,468	
October, 2022	November, 2022	\$3,125,680		\$3,125,680	
November, 2022	December, 2022	\$2,967,132	\$8,945	\$2,976,077	
December, 2022	January, 2023	\$3,306,328		\$3,306,328	\$2,969,946 24 mo
January, 2023	February, 2023	\$2,665,277		\$2,665,277	\$2,969,946 12 mo
TOTAL RECEIVED TO D	ATE	\$20,780,675	\$8,945	\$20,789,620	\$2,969,946 7 mo

ESPLOST 6 runs from July, 2022 to June, 2027 The tax is to raise not more than \$175m Planning was based on receipts of \$2m per month

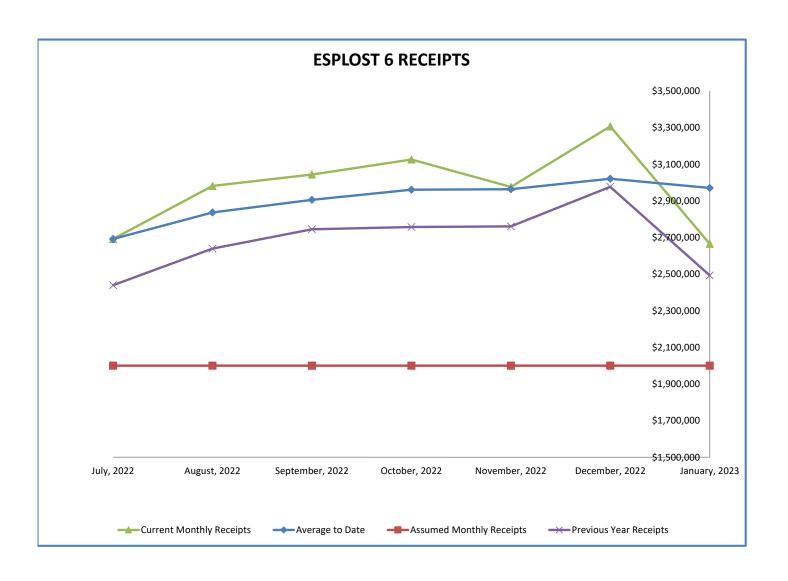

## ESPLOST 6 BUDGET PROJECTIONS AT FEBRUARY 28, 2023

Notes	Project	Original Budget	Projected Budget	t Expenditure	Encumbered	Remaining
Notes		Original Buuget			Eliculibeleu	Balance
1	Clarke Middle School	25,000,000	50,000,000	992	844,600	49,154,408
	Cedar Shoals	24,000,000	24,000,000	0	100,000	23,900,000
	Technology	22,000,000	22,000,000	3,136,301	118,234	18,745,465
2	Transportation	2,500,000	5,000,000	0	463,359	4,536,641
	Custodial Equipment	300,000	300,000	0	0	300,000
	School Nutrition	300,000	300,000	0	0	300,000
	Administration	1,950,000	1,933,348	231,565	95	1,701,688
Complete	ed projects I					
Projects n	I not yet commenced					
	Gaines	17,000,000	17,000,000	0	0	17,000,000
	Alps	11,000,000	11,100,000	0	0	11,100,000
	Cleveland	8,500,000	0	0	0	0
	Systems Renewal	4,000,000	4,000,000	0	0	4,000,000
2	Software Subscriptions	500,000	0	0	0	0
	Contingency	5,850,000	6,556,271	0	0	6,556,271
	PROJECT EXPENDITURE	122,900,000	142,189,619	3,368,858	1,526,287	137,294,473
				Received		
3	Capital Outlay Income	2,900,000	4,800,000	0		
4	Sales tax	120,000,000	137,389,619	20,789,619		
	INCOME	122,900,000	142,189,619	20,789,619		

- An additional \$14.13m was allocated from ESPLOST 5 to Clarke Middle School
- 2 Software subscriptions re-allocated to Transportation Bus Purchases
- 3 Projected Capital Outlay income based on:

Projected Received

Cedar Shoals 4,800,000 0

4 Sales tax income based on:

Original 60 months @ \$2,000,000 = \$120,000,000

Projected Received for the first seven months \$20,789,619

53 months @ \$2,200,000: \$116,600,000

TOTAL \$137,389,619

ESPLOST 6 runs from July, 2022 to June, 2027 The tax is to raise not more than \$175m
