

SPLOST MONTHLY REPORT

2/1/2024

1. Change Order Report

- Revised monthly report (see 1-page attachment)

2. Construction & Design Schedule

- Revised pre-construction schedule (see 1-page attachment)

3. Current Construction

- **West Broad Street Campus**

- Dr. Hooker and the Board are reviewing the District needs, ACC and community requests for the best use of West Broad Campus.

- **Clarke Middle School**

- General Contractor construction contract approved by the Board at the December 15th, 2022 BOE meeting with Grahl Construction for the amount of \$55,825,544
- Submittals for electrical switchgear and panels have been submitted and approved for order. Lead time is 72 weeks
- Phase 1 Clearing and Grubbing activities complete
- Excavation for building pad and retaining walls is complete
- Phase 1 Footing installation is complete for the 3 story structure
- Phase 1 underground plumbing is complete
- Phase 1 underground electrical is complete
- Phase 1 slab 100% poured
- Structural Steel installation of 3 story building is complete
- 3 story building roof truss and metal decking installation is complete
- 3 story building metal roof insulation and waterproofing in progress
- 3 story building CMU exterior masonry wall installation is complete
- 3 story exterior CMU wall damp proofing complete
- 3 story exterior brick masonry is 98% complete
- Kitchen, Cafeteria, Media Center slab is complete
- Kitchen, cafeteria media center structural steel complete
- Kitchen, Cafeteria, Media Center CMU walls complete
- Kitchen, cafeteria and media center roof 95% complete
- Gym locker room partial slab on grade has been poured
- Gym locker room structural steel complete
- Gym locker room CMU 99% complete
- Utility coordination held with GA Power, Atlanta Gas Light and ATT for Summer 2024 occupancy
- GA Power to run new feed to CMS week of 1-29-24

- **Cedar Shoals Renovation-Phase 1**

- CM at Risk contract with Carroll Daniel Construction approved at August board meeting
- Phase 1 drawings are complete with RFP issue date of October 24, 2023, bids for Demolition and HVAC work submitted December 16, 2023. GMP amendment for demo and HVAC approved by the Board at the January 2024 meeting
- Modular units for 9th grade and CTAE have been installed and occupied by staff and students
- Carroll Daniel on site with interior demo in progress lower level West side
- AG Science/Old fieldhouse empty, interior demo in progress

- **Upcoming projects in design**

- HVAC upgrades at Gaines, Johnnie Lay Burks, Bettye Henderson, Clarke Central and Winterville
- ACCA Bio Manufacturing Lab
- Projector & White Board replacement (15 Schools)
- WR Coile & ACCA Health Clinics

**SPLOST
Contingency / Change Order Report**

Contingency / Change Orders	ELC	Cedar Shoals	Clarke	ACCA
	Lastside at Old Gaines	Fieldhouse	Middle	Culinary
Established Budget By	RFQ	RFP	RFP	RFP
Approved Guaranteed Maximum Price or Bid		\$5,539,125.00	\$55,825,544.00	\$2,066,000.00
Original Contract Amount	\$2,000,000.00	\$5,539,125.00	\$55,825,544.00	\$2,066,000.00
Executed Change Orders: #1- 9/14/23			\$280,568.00	
Total Change Orders	\$0.00	\$0.00	\$280,568.00	\$0.00
Percentage of Contract Amount	0.00%	0.00%	0.50%	0.00%
Revised Contract Amount	\$2,000,000.00	\$5,539,125.00	\$56,106,112.00	\$2,066,000.00

SPLOST Construction & Design Schedule

The intent of this document is to provide anticipated and realized schedules of the current and upcoming SPLOST construction projects

February 1, 2024

Projects	Current Stage	Advertise By	Pre-Bid Conference	Bids Due	Notification to BOE *
Clarke Middle School	Construction	11/01/22	11/10/22	12/01/22	12/15/22
Cedar Shoals High School Renovation Phase 1	Bid	10/24/23	11/07/23	12/07/23	02/08/24
HVAC Upgrades-Gaines, Johnnie Lay Burks (Chase), Bettye H Holston (Alps), Clarke Central, Winterville	Design	01/26/24	TBD	02/27/24	03/21/24
ACCA Bio Manufacturing Lab	Design	12/15/23	01/15/24	01/23/24	02/08/24
Projector & White Board Replacement	Design	01/24/24	02/14/24	02/27/24	03/21/24
WR Coile & ACCA Health Clinics	Design	TBD	TBD	TBD	TBD
Cedar Shoals High School Renovation Phase 2	Design	TBD	TBD	TBD	TBD

* DATES INDICATED ARE ESTIMATES UNTIL PROGRAMMING AND INITIAL DESIGN PHASES ARE COMPLETE

Legend:

Active	Completed	Future
--------	-----------	--------

CLARKE COUNTY SCHOOL DISTRICT

ESPLOST 5 CONSTRUCTION PROGRAM

SCHEDULE OF INVESTMENT ACTIVITY

Month Ending December, 2023

	ESP5 Activity	Synovus Checking
Balance Ending November 30, 2023		\$11,863,432
<u>Earnings:</u>		
Interest Earnings - December 31, 2023		\$50,526
TOTAL REVENUES \$50,526		
<u>Expenditures:</u>		
Clarke Central Roof-Architect	\$4,180	
Culinary Kitchen-Expendable Equipment	\$7,882	
Culinary Kitchen-Construction	\$6,112	
Old Gaines Roof-Architect	\$5,748	
TOTAL EXPENDITURES \$23,921		
ACCOUNT TOTALS - December 31, 2023		\$11,890,037

ESPLOST 5 BUDGET PROJECTIONS AT DECEMBER 31, 2023

Notes	Project	Original Budget	Projected Budget	Expenditure	Encumbered	Remaining Balance
1	Cedar Shoals Field-House	0	6,428,643	6,401,788	26,855	0
	Clarke Central Roof	0	737,724	737,724	0	0
	Old Gaines Roof	0	688,628	683,546	2,925	2,157
	Clarke Middle	10,000,000	14,130,850	11,689,479	2,441,371	0
	HT Edwards Culinary Kitchen	0	2,289,960	1,842,448	412,246	35,266
	School Nutrition	300,000	300,000	159,705	107,784	32,511
	Coile Replacement Generator	0	49,990	0	49,990	0
	HB Stroud Fire Alarm	0	42,070	0	42,070	0
Completed Projects						
2	Administration	2,500,000	1,734,021	1,734,021	0	0
	BHL - Mar 2019	10,000,000	17,042,109	17,042,109	0	0
	Board HQ - Exploring Properties	0	23,209	23,209	0	0
	Board HQ -Prince Av. Purchase	0	5,517,956	5,517,956	0	0
	Board HQ - Prince Av. Renovation	0	8,412,680	8,412,680	0	0
	Cedar Shoals Old Gym - Jul 2020	0	528,948	528,948	0	0
	Cedar Shoals Track - Mar, 2021	2,000,000	1,043,345	1,043,345	0	0
	Clarke Central Softball - Sep 2019	0	446,263	446,263	0	0
	Clarke Central Softball Dugout	0	56,059	56,059	0	0
	Clarke Central Track/Field - Mar, 2021	0	5,283,087	5,283,087	0	0
	Coile - Mar 2019	10,000,000	16,162,136	16,162,136	0	0
	Cosmetology Lab - Dec 2019	0	292,260	292,260	0	0
	Custodial Equipment	300,000	299,549	299,549	0	0
	ELC Kitchen - May 2022	0	1,018,607	1,018,607	0	0
	Gaines Kitchen Floor - Jul 2019	0	39,016	39,016	0	0
	Hilsman - Sep 2019	25,000,000	28,082,480	28,082,480	0	0
	Hilsman Health Clinic - Sep 2019	0	171,666	171,666	0	0
	HS Basketball Scoreboards	0	62,792	62,792	0	0
	Manufacturing Lab - Feb 2021	0	467,733	467,733	0	0
	Oglethorpe - Sep 2018	5,000,000	1,511,918	1,511,918	0	0
	Old Gaines - ELC	0	1,071,484	1,071,484	0	0
	Plant Services Truck	0	25,160	25,160	0	0
	Property Assessments	121,098	121,098	121,098	0	0
	Public Safety Radio - Dec 2020	0	138,505	138,505	0	0
	Storefronts - Sep 2019	0	71,964	71,964	0	0
Systems Renewal	8,425,000	346,699	346,699	0	0	
Technology	20,000,000	18,005,177	18,005,177	0	0	
Transportation - Buses	2,500,000	2,473,000	2,473,000	0	0	
Projects not yet commenced						
5	Cedar Shoals - Systems	0	0	0	0	0
	District Services	1,700,000	22,707	22,707	0	0
	Extra Curricular	2,500,000	0	0	0	0
	Old Gaines	0	5,193	5,193	0	0
	School C	0	4,620	4,620	0	0
	Timothy Road	2,500,000	0	0	0	0
	West Broad for ELC	6,000,000	414,131	414,131	0	0
	Contingency	2,153,902	9,691,135	0	0	9,691,135
	PROJECT EXPENDITURE	111,000,000	145,254,572	132,410,261	3,083,242	9,761,069
			Received to Date			
6	Capital Outlay Income	0	9,812,240	9,812,240		
3	Piedmont-Hilsman Clinic	0	171,666	171,666		
7	Sales tax	111,000,000	135,270,665	135,270,665		
	INCOME	111,000,000	145,254,571	145,254,571		

Notes

- 1 \$14.13m allocated from ESPLOST 5 to Clarke Middle School new-build. The balance required will be met from ESPLOST 6
- 2 Additional funds of \$2.7m used from the Capital Project Fund 370
- 3 The Hilsman Health Clinic work was managed by the SPLOST Department but not ESPLOST funded. Funding was from the Piedmont Health Foundation
- 4 Oglethorpe was predominantly funded from ESPLOST 4 - \$19,467,684
- 5 Extra Curricular funds were re-allocated to High School Athletics

6 **Capital Outlay income:**

	Projected	Received
BHL	1,728,088	1,728,088
Coile	2,343,006	2,343,006
Hilsman	5,741,146	5,741,146
TOTAL	9,812,240	9,812,240

7 **Sales tax income based on:**

Original	60 months @ \$1,850,000 = \$111,000,000	
FINAL	Received for the 60 months:	\$135,270,665

ESPLOST 5 ran from July, 2017 to June, 2022

CLARKE COUNTY SCHOOL DISTRICT
ESPLOST 6 CONSTRUCTION PROGRAM
SCHEDULE OF INVESTMENT ACTIVITY
Month Ending December, 2023

	ESP6 Activity	Synovus Checking	Synovus Custodial	Invested
Balance Ending November 30, 2023		\$2,079,791	\$6,528,124	\$82,943,319
<u>Earnings:</u>				
Interest Earnings/Gains - December 31, 2023		\$15,004	\$13,450	\$338,411
Sales Tax - October, 2023				\$3,208,294
Sales Tax - November, 2023				\$5,932
TOTAL REVENUES \$3,581,091				
<u>Expenditures:</u>				
Administration-Payroll	\$25,151			
Administration-Travel	\$361			
Administration-Copier Charges	\$27			
Administration-Office Supplies	\$10			
Cedar Shoals-Architect	\$104,422			
Cedar Shoals-Expendable Equipment	\$9,150			
Cedar Shoals-Construction	\$32,621			
Cedar Shoals-Rental of Equipment	\$20,570			
Cedar Shoals-Other Purchased Services	\$1,829			
Clarke Middle-Architect	\$84,971			
Clarke Middle-Engineering	\$18,455			
Clarke Middle-Rental of Equipment	\$49,555			
Clarke Middle-Construction	\$4,570,417			
Technology	\$12,737			
TOTAL EXPENDITURES \$4,930,277				
<u>Transfers & Adjustments</u>				
Transfer			\$30,699	-\$30,699
Transfer		\$4,800,000	-\$4,800,000	
ACCOUNT TOTALS - December 31, 2023		\$1,630,320	\$1,772,273	\$86,465,257
TOTAL ESPLOST 6 CASH AND INVESTMENTS				\$89,867,849


CLARKE COUNTY SCHOOL DISTRICT

ESPLOST 6 CONSTRUCTION PROGRAM

SCHEDULE OF SALES TAX RECEIPTS - Month Ending December, 2023

MONTH COLLECTED	MONTH RECEIVED	ESPLOST Sales Tax Receipt	ESPLOST Pro-Rata	Current Monthly Receipts	Averages
July, 2022	September, 2022	\$2,691,547		\$2,691,547	
August, 2022	October, 2022	\$2,981,243		\$2,981,243	
September, 2022	November, 2022	\$3,043,468		\$3,043,468	
October, 2022	December, 2022	\$3,125,680		\$3,125,680	
November, 2022	January, 2023	\$2,967,132	\$8,945	\$2,976,077	
December, 2022	February, 2023	\$3,306,328		\$3,306,328	
January, 2023	March, 2023	\$2,665,277		\$2,665,277	
February, 2023	May, 2023	\$2,685,663		\$2,685,663	
March, 2023	June, 2023	\$3,018,583		\$3,018,583	
April, 2023	July, 2023	\$2,912,335	\$6,651	\$2,912,335	
May, 2023	August, 2023	\$2,978,174		\$2,984,825	
June, 2023	September, 2023	\$2,939,878		\$2,939,878	
July, 2023	October, 2023	\$3,107,953		\$3,107,953	
August, 2023	November, 2023	\$3,252,210		\$3,252,210	
September, 2023		\$3,407,688		\$3,407,688	
October, 2023		\$3,208,294		\$3,208,294	
November, 2023		\$3,172,535	\$5,932	\$3,178,467	
TOTAL RECEIVED TO DATE		\$51,463,988	\$21,528	\$51,485,516	\$3,055,625 12 mo

ESPLOST 6 runs from July, 2022 to June, 2027
 The tax is to raise not more than \$175m
 Planning was based on receipts of \$2m per month

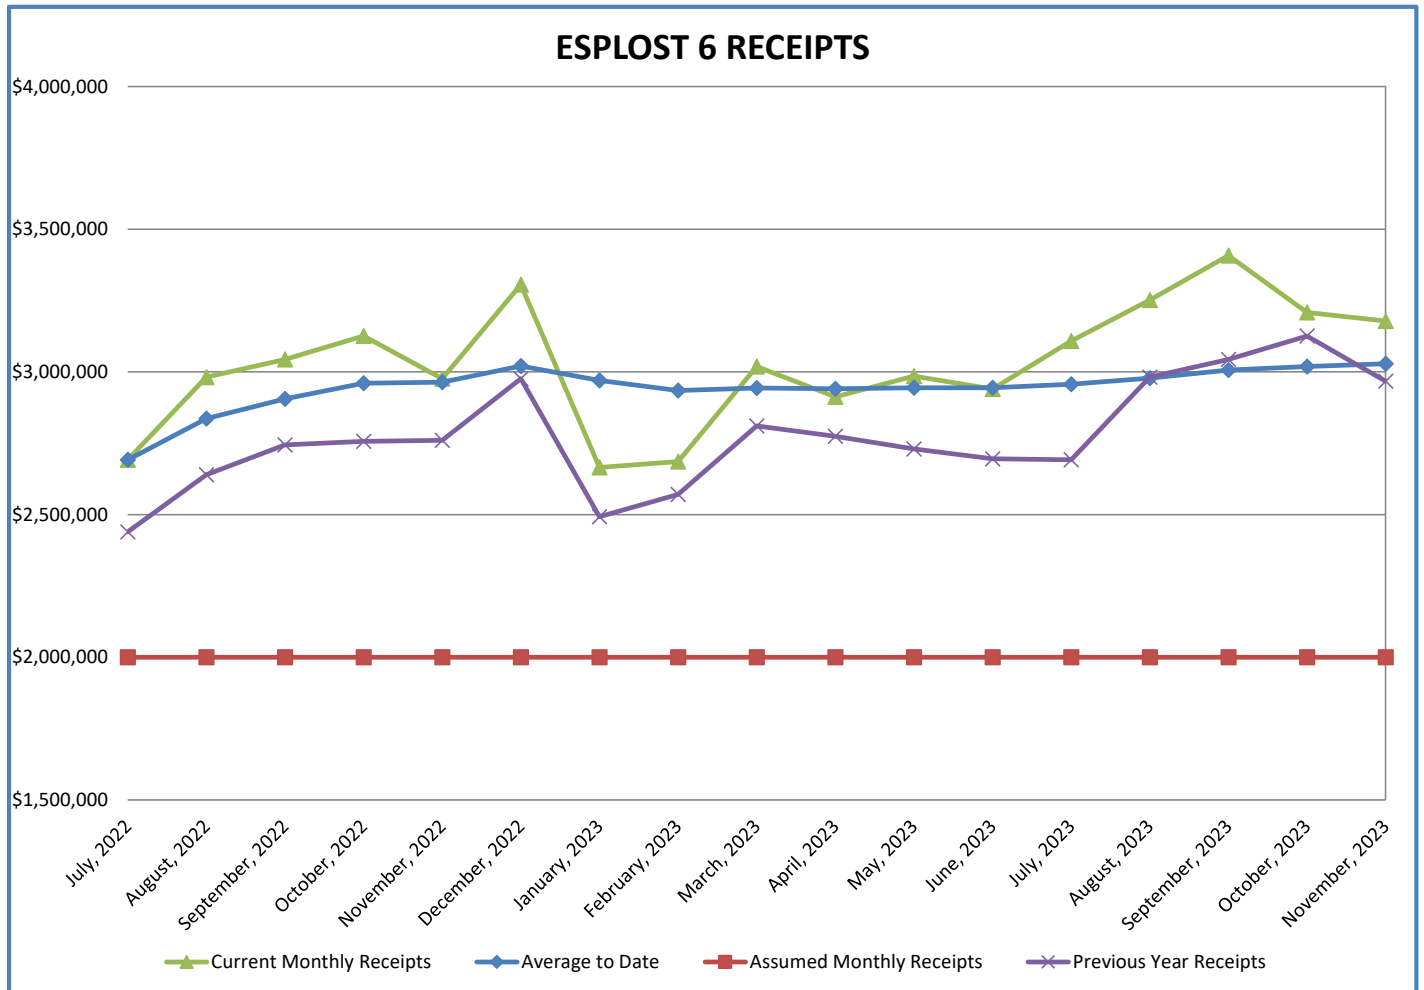

ESPLOST 6 BUDGET PROJECTIONS AT DECEMBER 31, 2023

Notes	Project	Original Budget	Projected Budget	Expenditure	Encumbered	Remaining Balance
1	Clarke Middle School	25,000,000	50,000,000	17,606,107	13,531,679	18,862,213
	Cedar Shoals	24,000,000	45,980,000	966,630	5,989,321	39,024,050
	Technology	22,000,000	22,000,000	4,044,306	5,170,174	12,785,521
2	Transportation	2,500,000	5,000,000	403,359	0	4,596,641
	Custodial Equipment	300,000	300,000	3,523	0	296,477
	School Nutrition	300,000	300,000	0	0	300,000
	Administration	1,950,000	1,863,605	513,474	3,089	1,347,041
Completed projects						
Projects not yet commenced						
	Gaines	17,000,000	17,000,000	0	0	17,000,000
	Alps	11,000,000	0	0	0	0
	Cleveland	8,500,000	0	0	0	0
	Systems Renewal	4,000,000	4,000,000	0	0	4,000,000
2	Software Subscriptions	500,000	0	0	0	0
	Contingency	5,850,000	8,741,911	0	0	8,741,911
	PROJECT EXPENDITURE	122,900,000	155,185,516	23,537,398	24,694,263	106,953,854
				Received		
3	Capital Outlay Income	2,900,000	4,800,000	0		
4	Sales tax	120,000,000	150,385,516	51,485,516		
	INCOME	122,900,000	155,185,516	51,485,516		

1 An additional \$14.13m was allocated from ESPLOST 5 to Clarke Middle School

2 Software subscriptions re-allocated to Transportation - Bus Purchases

3 **Projected Capital Outlay income based on:**

	Projected	Received
Cedar Shoals	4,800,000	0

4 **Sales tax income based on:**

Original Assumption: 60 months @ \$2,000,000 = \$120,000,000
 Current Assumption: \$2,300,000 per month

Projected	Received for the first 17 months	\$51,485,516
	43 months @ \$2,300,000:	\$98,900,000

TOTAL **\$150,385,516**

ESPLOST 6 runs from July, 2022 to June, 2027

The tax is to raise not more than \$175m
